



2024 Johnson Creek Gosdeck Crossing Construction Weekly Construction Update Update #18 (9/13/2024)

Work Completed Week of Starting: 9/9/2024 Ending: 9/13/2024

- Bridge diaphragm construction.
- Bridge deck pouring.
- Bridge deck curing.

Work Scheduled for Week of Starting: 9/16/2024

- Bridge sidewalk forming and pouring.
- Parapet forming.

Estimated Contract Completion Date: 06/13/2025

Village Engineer Contact Information: Christian Moring 262-665-3012 <u>christian.moring@stantec.com</u>

Resident Engineer Contact Information: Bill Davis 608-621-0533 <u>William.Davis@stantec.com</u>

Village Contact Information: Kyle Ellefson 920-699-2296 villageadministrator@vi.johnsoncreek.wi.gov

Ending: 9/20/2024




Village Of Johnson Creek






Concrete Deck Pour







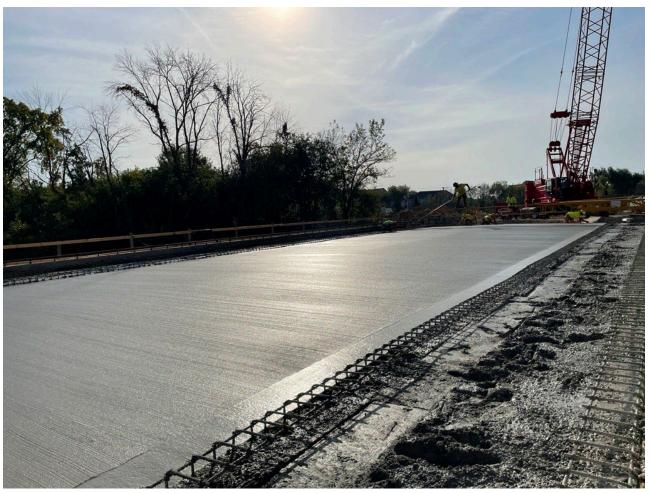

Finished Concrete Deck Before Curing.
