



2024 Johnson Creek Gosdeck Crossing Construction Weekly Construction Update Update #16 (8/30/2024)

Work Completed Week of Starting: 8/26/2024 Ending: 8/30/2024

- Bearing pad setting
- Bridge girders and diaphragm setting.
- Bridge deck forming.

Work Scheduled for Week of Starting: 9/2/2024

- Bridge deck reinforcement setting.
- Bridge deck forming.
- Bridge deck pouring.

Estimated Contract Completion Date: 06/13/2025

Village Engineer Contact Information: Christian Moring 262-665-3012 <u>christian.moring@stantec.com</u>


Resident Engineer Contact Information: Bill Davis 608-621-0533 <u>William.Davis@stantec.com</u>

Village Contact Information: Kyle Ellefson 920-699-2296 <u>villageadministrator@vi.johnsoncreek.wi.gov</u> Ending: 9/6/2024







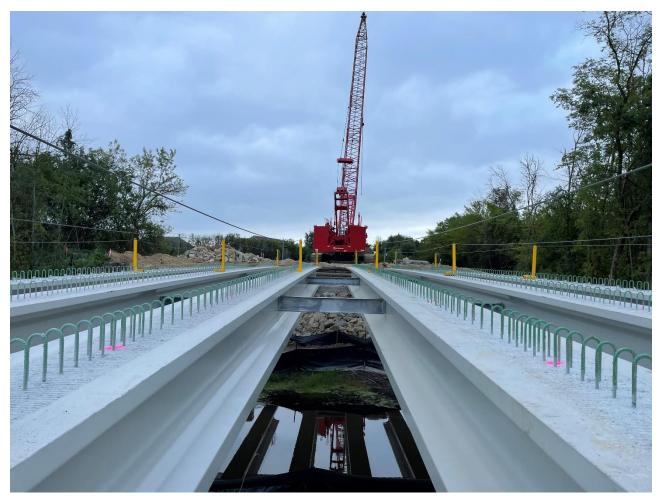

Installed girders from the north side.



Village Of Johnson Creek





Preliminary deck formwork.
